



ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors	% Complete
155		Door Frame Delivery	0 days	Wed 24-07-03	Wed 24-07-03	152		0%
156		Interior Fit-up and Rough Inn	121 days	Thu 24-02-22	Thu 24-08-15			9%
157		Interior Rough Inns B2	50 days	Thu 24-02-22	Fri 24-05-03			38%
158		HVAC & Mechanical	50 days	Thu 24-02-22	Fri 24-05-03	122	159SS,160SS,161	40%
159		Electrical	20 days	Thu 24-02-22	Thu 24-03-21	158SS		40%
160		Fire Protection	20 days	Thu 24-02-22	Thu 24-03-21	158SS		70%
161		Elevator Machine Rooms	20 days	Thu 24-02-22	Thu 24-03-21	158SS		0%
162		Installation of housekeeping pads	3 days	Thu 24-02-22	Tue 24-02-27	158SS		50%
163		Interior Rough Inns B1	30 days	Thu 24-02-22	Fri 24-04-05			14%
164		HVAC & Mechanical	20 days	Thu 24-02-22	Thu 24-03-21	122	171	0%
165		Electrical	20 days	Thu 24-02-22	Thu 24-03-21	122	172	50%
166		Fire Protection	20 days	Thu 24-02-22	Thu 24-03-21	122	173	0%
167		Elevator Shaft and Inserts	20 days	Thu 24-02-22	Thu 24-03-21	122	169,174	0%
168		Installation of housekeeping pads	3 days	Thu 24-02-22	Tue 24-02-27	122		100%
169		Car elevator Installation	10 days	Thu 24-03-21	Fri 24-04-05	103,76,167		0%
170		Interior Rough Inns Ground Floor	40 days	Tue 24-05-21	Wed 24-07-17	149		7%
171		HVAC & Mechanical	20 days	Tue 24-05-21	Tue 24-06-18	164	176SS,178FS-1	0%
172		Electrical	20 days	Tue 24-05-21	Tue 24-06-18	165	179FS-10 days	25%
173		Fire Protection	20 days	Tue 24-05-21	Tue 24-06-18	166	180FS-10 days	0%
174		Elevator Shaft and Inserts	20 days	Tue 24-05-21	Tue 24-06-18	167	181FS-10 days	0%
175		Stair Construction Ground Floor to 4th Floor North and South	40 days	Tue 24-05-21	Wed 24-07-17	149	204	0%
176		Wall Layouts and framing	10 days	Tue 24-05-21	Tue 24-06-04	171SS	182	40%
177		Interior Rough Inns Level 1	20 days	Tue 24-06-04	Wed 24-07-03			0%
178		HVAC & Mechanical	20 days	Tue 24-06-04	Wed 24-07-03	171FS-10 da	184FS-10 days	0%
179		Electrical	20 days	Tue 24-06-04	Wed 24-07-03	172FS-10 da	185FS-10 days	0%
180		Fire Protection	20 days	Tue 24-06-04	Wed 24-07-03	173FS-10 da	186FS-10 days	0%
181		Elevator Shaft and Inserts	20 days	Tue 24-06-04	Wed 24-07-03	174FS-10 da	187FS-10 days	0%
182		Wall Layouts and framing	10 days	Tue 24-06-04	Tue 24-06-18	176	188	0%
183		Interior Rough Inns Level 2	20 days	Tue 24-06-18	Wed 24-07-17			0%
184		HVAC & Mechanical	20 days	Tue 24-06-18	Wed 24-07-17	178FS-10 da	190FS-10 days	0%
185		Electrical	20 days	Tue 24-06-18	Wed 24-07-17	179FS-10 da	191FS-10 days	0%
186		Fire Protection	20 days	Tue 24-06-18	Wed 24-07-17	180FS-10 da	192FS-10 days	0%
187		Elevator Shaft and Inserts	20 days	Tue 24-06-18	Wed 24-07-17	181FS-10 da	193FS-10 days	0%
188		Wall Layouts and framing	10 days	Tue 24-06-18	Wed 24-07-03	182	194	0%
189		Interior Rough Inns Level 3	20 days	Wed 24-07-03	Wed 24-07-31			0%
190		HVAC & Mechanical	20 days	Wed 24-07-03	Wed 24-07-31	184FS-10 da	196FS-10 days	0%

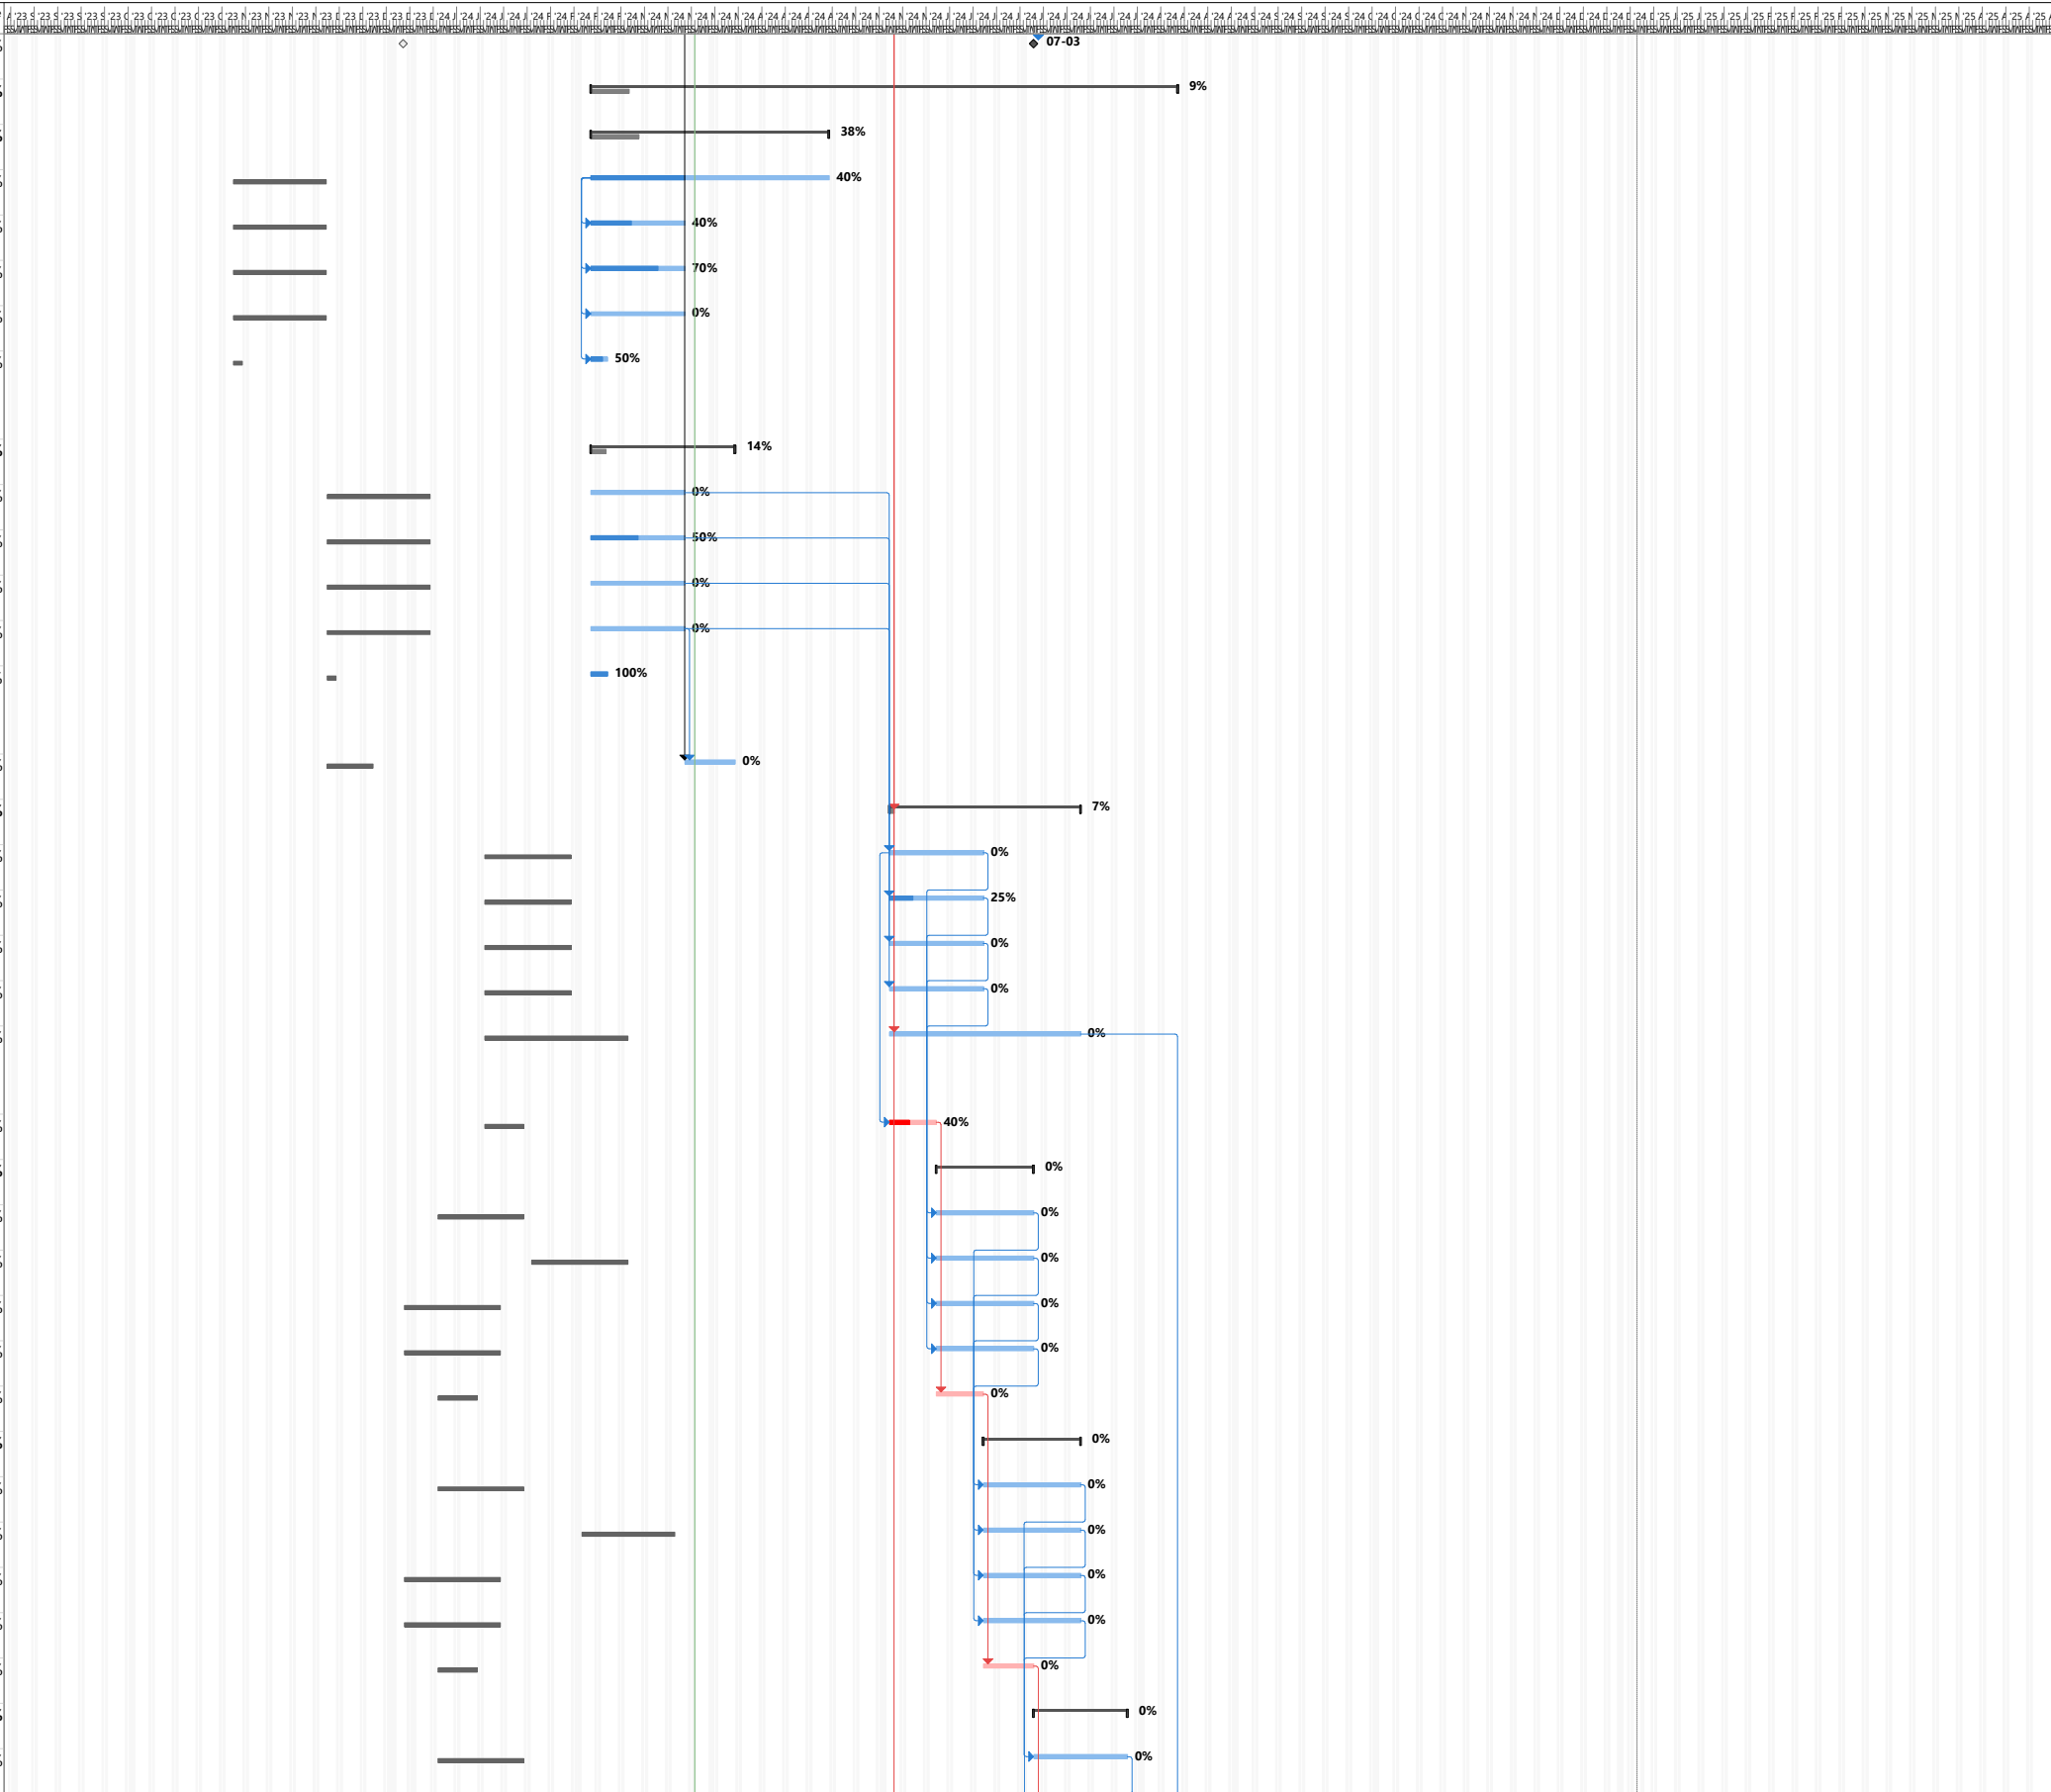

Critical Critical Progress Split Manual Task Finish-only Baseline Baseline Milestone Summary Progress Manual Summary External Tasks Inactive Task Inactive Summary
Critical Split Task Task Progress Start-only Duration-only Baseline Split Milestone Summary Project Summary External Milestone Inactive Milestone Deadline

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors	% Complete
191		Electrical	20 days	Wed 24-07-03	Wed 24-07-31	185FS-10 da	197FS-10 days	0%
192		Fire Protection	20 days	Wed 24-07-03	Wed 24-07-31	186FS-10 da	198FS-10 days	0%
193		Elevator Shaft and Inserts	20 days	Wed 24-07-03	Wed 24-07-31	187FS-10 da	199FS-10 days	0%
194		Wall Layouts and framing	10 days	Wed 24-07-03	Wed 24-07-17	188	200	0%
195		Interior Rough Inns Level 4	20 days	Wed 24-07-17	Thu 24-08-15			0%
196		HVAC & Mechanical	20 days	Wed 24-07-17	Thu 24-08-15	190FS-10 da		0%
197		Electrical	20 days	Wed 24-07-17	Thu 24-08-15	191FS-10 da		0%
198		Fire Protection	20 days	Wed 24-07-17	Thu 24-08-15	192FS-10 da		0%
199		Elevator Shaft and Inserts	20 days	Wed 24-07-17	Thu 24-08-15	193FS-10 da		0%
200		Wall Layouts and framing	10 days	Wed 24-07-17	Wed 24-07-31	194	204,202	0%
201		Floors, Finishes and Fixtures	90 days	Wed 24-07-31	Mon 24-12-09			0%
202		Infloor Heating Loops Installation	10 days	Wed 24-07-31	Thu 24-08-15	200	203FS-10 days	0%
203		Floor topping over infloor heat	10 days	Wed 24-07-31	Thu 24-08-15	202FS-10 da	204	0%
204		drywall	3 wks	Thu 24-08-15	Fri 24-09-06	200,203,175	205	0%
205		Prime and Paint One Coat	15 days	Fri 24-09-06	Fri 24-09-27	204	206,207,208,209	0%
206		Electrical Fixtures	20 days	Fri 24-09-27	Mon 24-10-28	205	228	0%
207		Plumbing Fixtures	20 days	Fri 24-09-27	Mon 24-10-28	205	228	0%
208		AV and Security	20 days	Fri 24-09-27	Mon 24-10-28	205	228	0%
209		Door and hardware installation	15 days	Fri 24-09-27	Mon 24-10-21	205	228	0%
210		Tile Installation	25 days	Fri 24-09-27	Mon 24-11-04	205	228	0%
211		Casework Installation	20 days	Fri 24-09-27	Mon 24-10-28	205	212	0%
212		Flooring Installation	25 days	Mon 24-10-28	Mon 24-12-02	205,211	213FS-10 days	0%
213		Final Paint	10 days	Mon 24-11-18	Mon 24-12-02	212FS-10 da	228,214	0%
214		Furniture and Appliance Installatio	5 days	Mon 24-12-02	Mon 24-12-09	213		0%
215		Exterior Works and services	100 days	Tue 24-05-21	Fri 24-10-11	149		0%
216		Excavation	5 days	Tue 24-05-21	Tue 24-05-28	122	217,218	0%
217		manholes	5 wks	Tue 24-05-28	Wed 24-07-03	216		0%
218		site work and services	5 wks	Tue 24-05-28	Wed 24-07-03	216	219	0%
219		Backfill and compaction	2 wks	Wed 24-07-03	Wed 24-07-17	218	220FS+40 days	0%
220		Concrete and masonry work	20 days	Fri 24-09-13	Fri 24-10-11	219FS+40 da	222SS	0%
221		Final Paving	5 days	Fri 24-10-04	Fri 24-10-11	223		0%
222		Re pointing of masonry	10 days	Fri 24-09-13	Fri 24-09-27	220SS	223,225	0%
223		Placement of Dormer and shutter	5 days	Fri 24-09-27	Fri 24-10-04	222	226,221	0%
224		Landscaping and Exterior Finishes	20 days	Fri 24-09-27	Mon 24-10-28			0%
225		Decorative masonry	10 days	Fri 24-09-27	Fri 24-10-11	222	226	0%
226		Plantings	2 wks	Fri 24-10-11	Mon 24-10-28	223,225	229	0%
227		Project Closeout and Commissioning	18 days	Mon 24-12-02	Mon 24-12-30			0%
228		Commisioning	1 wk	Mon 24-12-02	Mon 24-12-09	213,206,207	229	0%

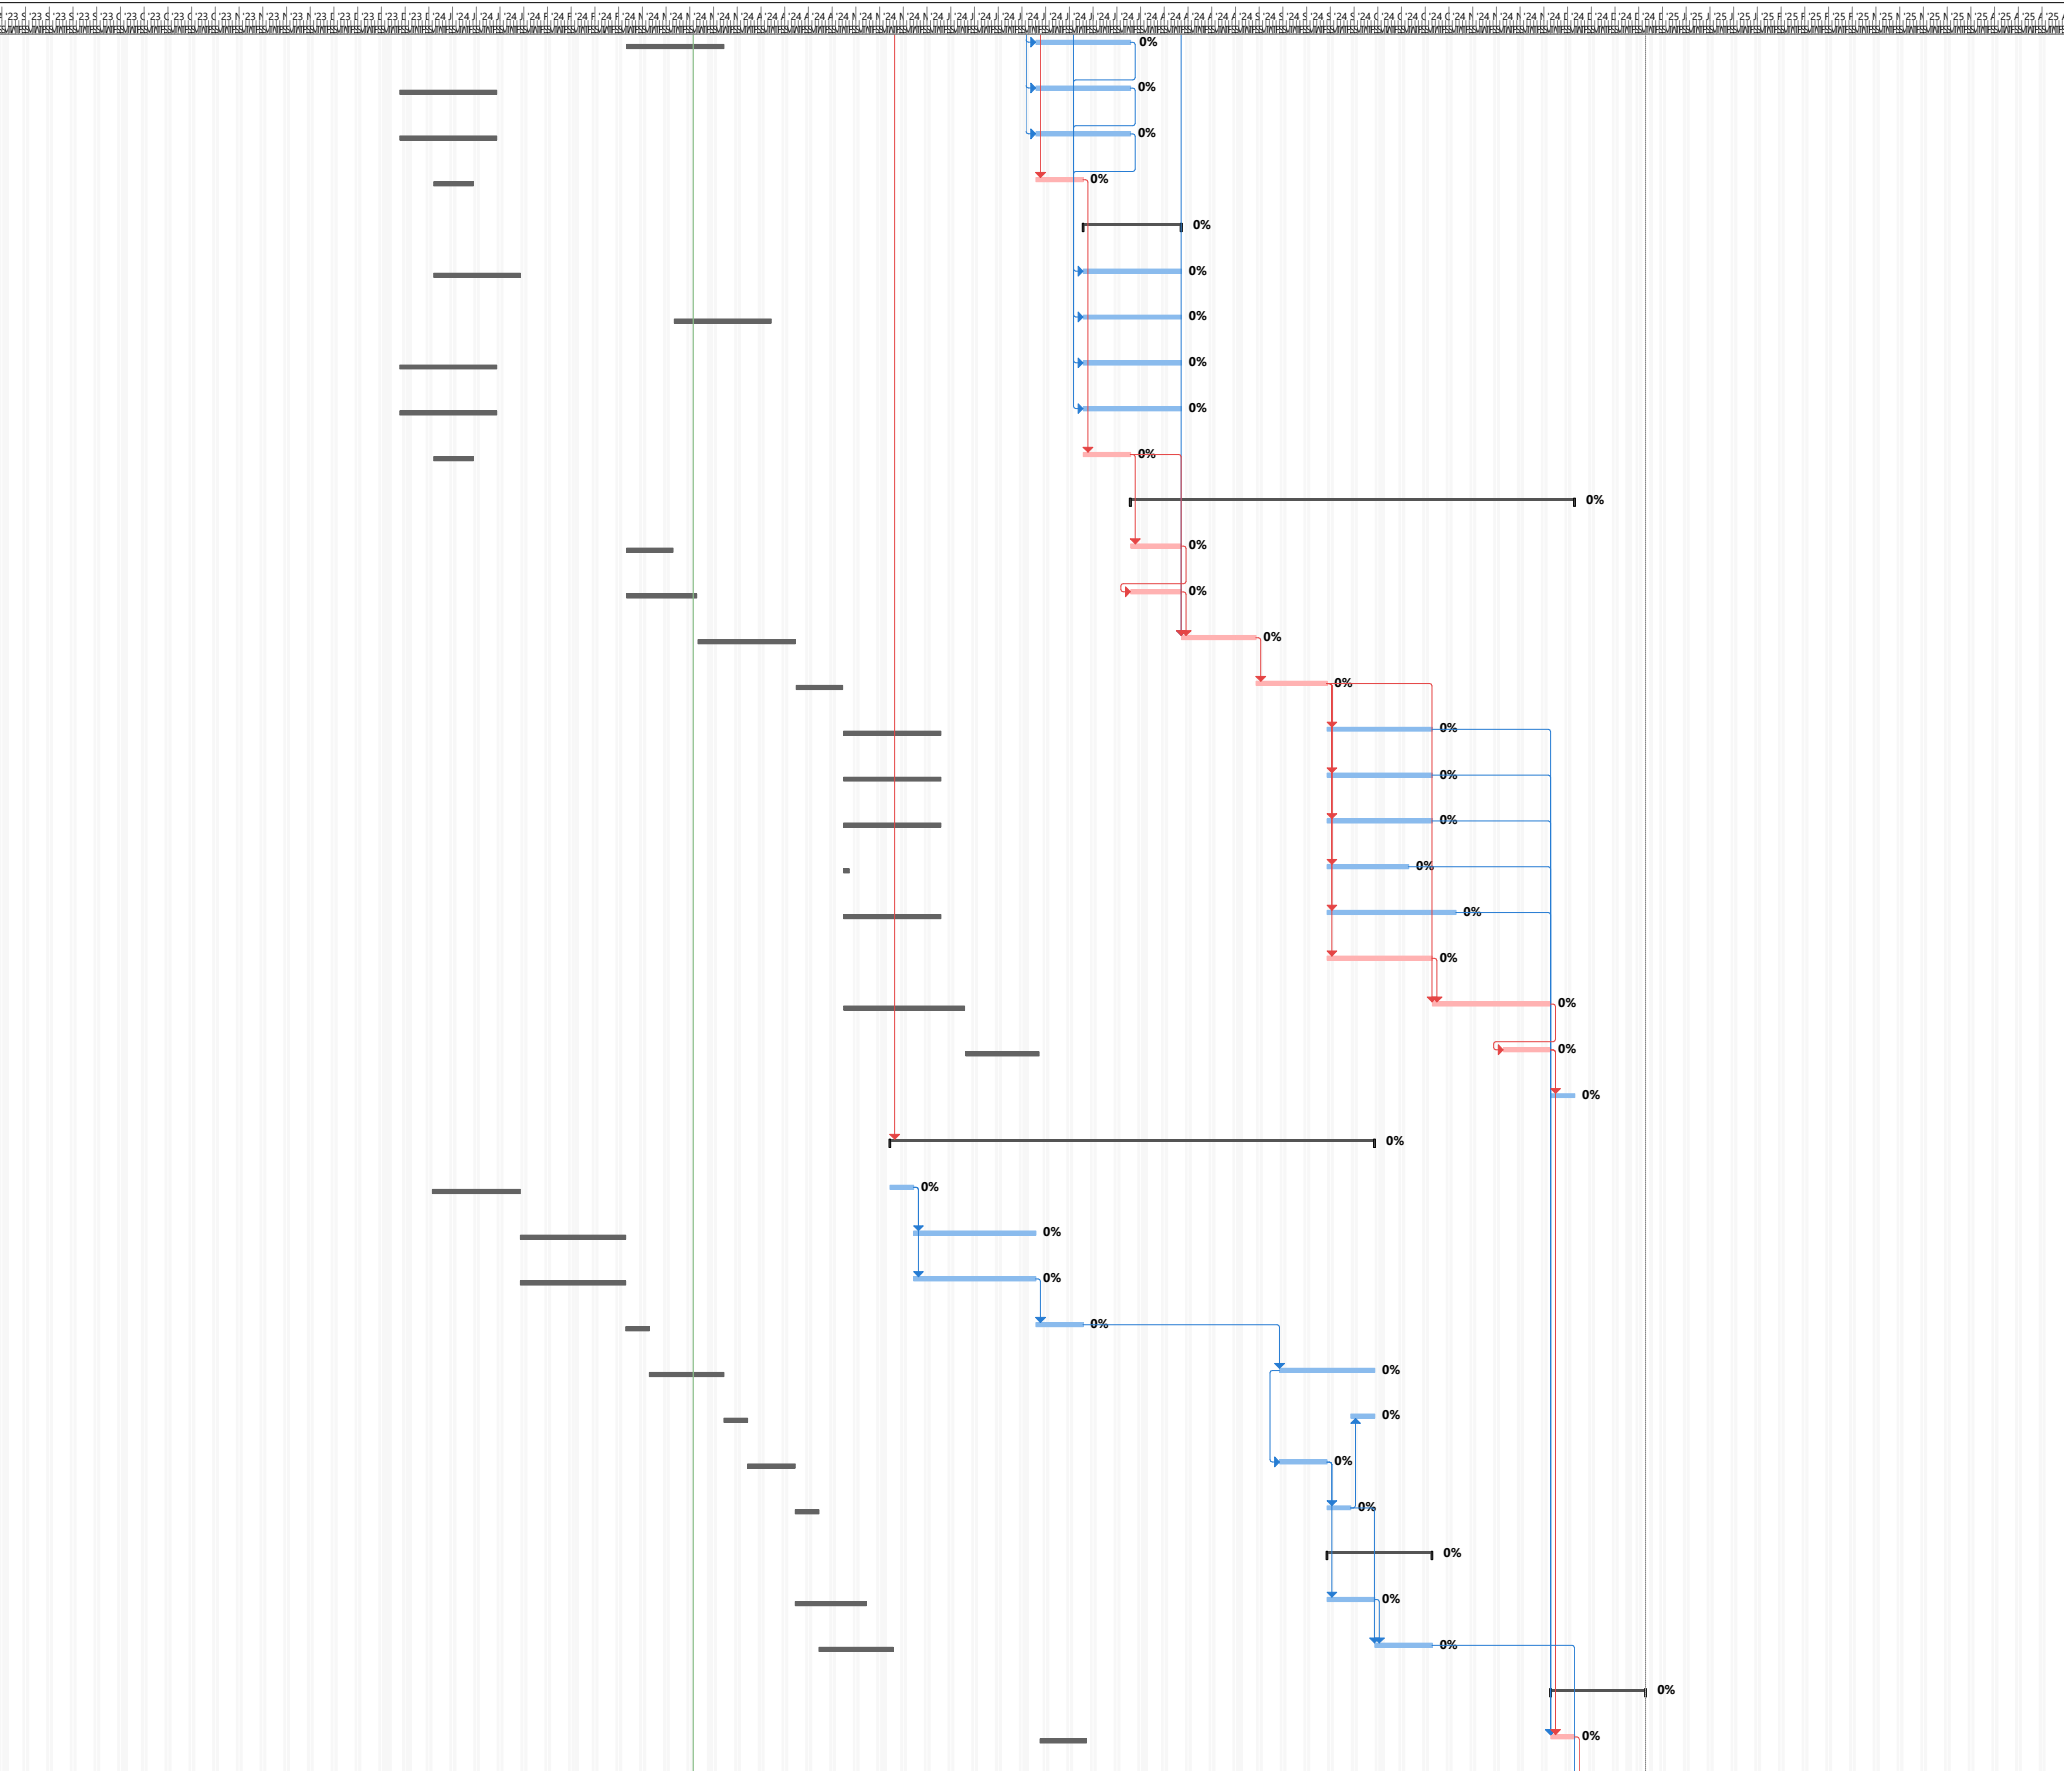

█ Critical
█ Critical Split
█ Critical Progress
█ Task Progress
█ Split
█ Task Progress
█ Manual Task
█ Start-only
█ Finish-only
█ Duration-only
█ Baseline
█ Baseline Split
█ Baseline Milestone
█ Milestone
█ Summary Progress
█ Summary
█ Manual Summary
█ Project Summary
█ External Tasks
█ External Milestone
█ Inactive Task
█ Inactive Milestone
█ Inactive Summary
█ Deadline

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors	% Complete
229		Training	3 days	Mon 24-12-09	Thu 24-12-12	228,226	230	0%
230		Deficiency Correction	2 wks	Thu 24-12-12	Mon 24-12-30	229	231	0%
231		Project complete	0 days	Mon 24-12-30	Mon 24-12-30	230		0%



Critical Critical Progress Split Manual Task Finish-only Baseline Baseline Milestone Summary Progress Manual Summary External Tasks Inactive Task Inactive Summary
 Critical Split Task Task Progress Start-only Duration-only Baseline Split Milestone Summary Project Summary External Milestone Inactive Milestone Deadline
